

PROPOSAL
TO THE
CITY OF CAMBRIDGE

from
R.G. WILSON & ASSOCIATES

TO PERFORM
A SEGMENT OF THE CITY'S
HIGH CRIME AREA SECURITY PROGRAM

July 12, 1971


R.G. WILSON & ASSOCIATES
10 CRESTSHIRE DRIVE, LAWRENCE, MASS. 01843 (617) 682-0738

TABLE OF CONTENTS

	<u>PAGE</u>
OVERVIEW	ii
SPECIAL NOTE	vi
METHODOLOGY	1 - 24
Task 2 - Area Analysis	1 - 10
2.1 Development of Area Knowledge	1
2.1.1 Demographic	1
2.1.2 Crime Patterns	2
2.1.3 Police Activity & Citizen- Police Attitude	3
2.1.4 Identification of Variables	4
2.2 Development of Data Base	5
2.3 Boundary Refinement	9
Task 3 - Resource Allocation Study	10 - 18
3.1 Available Resource Survey	10 - 18
3.2 Short-range Adjustments	10 - 14
3.3 Additional Study Specifica- tion	10, 18
Task 4 - Reduction Technique Inventory	19,-20
Task 5 - Experiment Planning	20
5.1 Technique Selection	20
5.1.1 Estimate of Effects	21
5.1.2 Establishment of Priorities	21
5.2 Planning	21
5.2.1 Controls	21
5.2.2 Measurement	22
5.2.3 Generalization of Results	22
5.2.4 Procedure	22
5.2.5 Setting-up and Settling-down	22
5.3 Continuation Funding	24
TIMETABLE	25 - 26
BUDGET SUMMARY	27

OVERVIEW

R.G. Wilson and Associates proposes to perform Tasks 2-5 as described in the Project Description for a High Crime Area Security Program (Project Number 70-20) submitted by the City of Cambridge to the Governor's Public Safety Committee. Those Tasks as well as the corresponding sequence and time expectations are illustrated in the following chart.

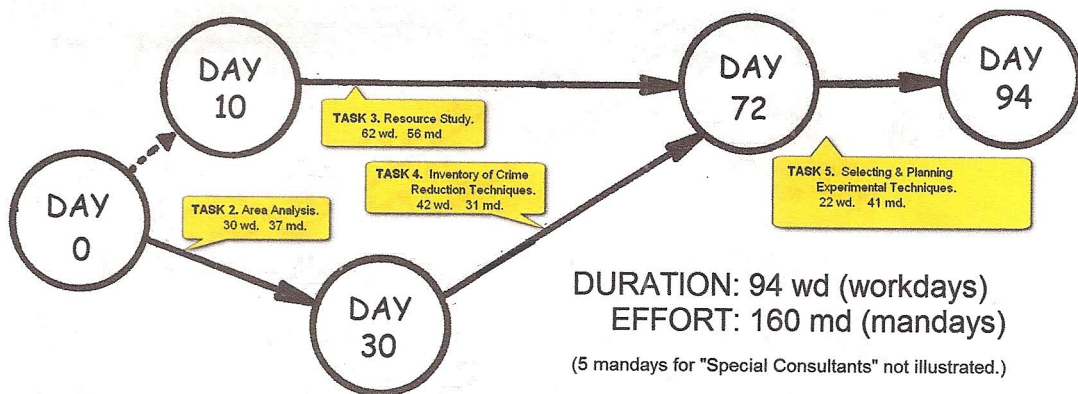

It is estimated that the performance of these tasks will require 1,280 hours on the part of a team particularly well qualified for such a project.

RAYMOND G. WILSON is the former Director of Planning and Research for the Quincy Police. His professional and academic background covers all areas of performance specified by Cambridge's Project Description. He holds a Bachelor's Degree with Honors in Sociology, having concentrated on Social Research Methods. He has designed and conducted two extensive sociological field studies (re: Task #2, Area Analysis), and prepared a detailed procedure for the analysis of police patrol methods. As a police employee, he was the project leader in the initial development stages of a police information system and the chief author of that project's

METHODOLOGY

The City's Project Description not only identifies the objectives of the project, but several components of the methodology as well. Those methodological components are all acceptable to the consultant and--assuming they are acceptable to the City--need not be reiterated here. The consultant accepts all the conditions, specifications, assistance, recommendations and directives made by the City in the Project Description. Accordingly, any elements of the project description not expressly mentioned in this proposal are still a part of the work plan. They have been omitted only to simplify the work of the proposal's evaluators.

Task 2 - Analysis of Area

Wilson	160 hours
McCarthy	56 hours
Angell	16 hours
Research Assist.	64 hours
TOTAL	296 hours

The City specified three objectives for this task.

Objective 2.1

"Develop detailed knowledge of the area required for planning of experimental crime reduction techniques."

To satisfy this objective, the consultant will prepare a four part description of the area.

2.1.1 Demographic


A sociological monograph will be prepared, detailing the habits, patterns, life styles, attitudes and economics of the population of the area. Included will be a physical description, an analysis of population flows, and the structure and patterns of the formal and informal subgroups both within and influencing the area.

PROJECT SCHEDULE

PROJECT DAY:




- Task 2 - Area Analysis
 - 2.1 Development of Area Knowledge
 - 2.1.1 Demographic
 - 2.1.2 Crime Patterns
 - 2.1.3 Police Activity & Citizen-Police Attitude
 - 2.1.4 Identification of Variables
 - 2.2 Development of Data Base
 - 2.3 Boundary Refinement

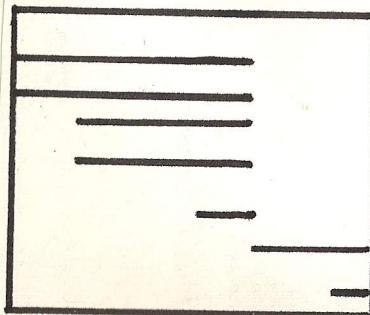

PROJECT DAY:




- Task 3 - Resource Allocation Study
 - 3.1 Available Resource Survey
 - 3.2 Short-range Adjustments
 - 3.3 Additional Study Specification



PROJECT DAY:



- Task 4 - Reduction Technique Inventory



- Task 5 - Experiment Planning
 - 5.1 Technique Selection
 - 5.1.1 Estimate of Effects
 - 5.1.2 Establishment of Priorities
 - 5.2 Planning
 - 5.2.1 Controls
 - 5.2.2 Measurement
 - 5.2.3 Generalization of Results
 - 5.2.4 Procedure
 - 5.2.5 Setting-up and Settling-down
 - 5.3 Continuation Funding

